




Amity School District

Dedicated To Excellence In Education

Capital Bond Program Newsletter

MARCH 2025

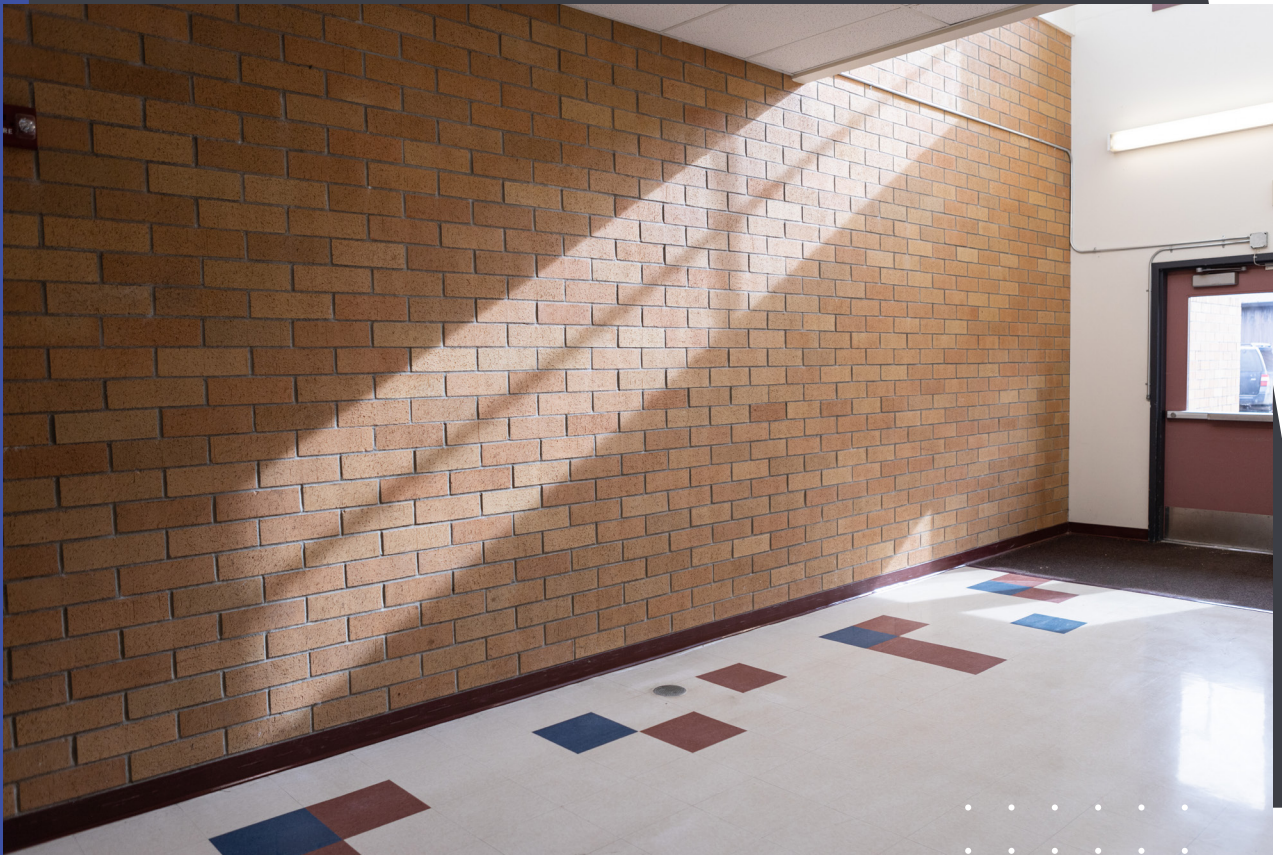

GENERAL PROGRAM UPDATE

Construction continues to move forward across the Amity School District Bond Program. With spring approaching, crews are focused on maintaining momentum and hitting key interior milestones at both the middle school classroom addition and the high school competition gymnasium.

This month, a decision was finalized on the graphics package for the new competition gym. This step moves the interior design forward and keeps the gym on track for final finishes.

The overall project remains on schedule. Teams are staying on top of known delays—mainly utility coordination issues—without affecting critical milestones. With over 200 activities complete and 24 currently active, the bond program is staying aligned with its construction goals heading into the final stretch.





CURRENT ACTIVITIES

Classroom Addition (Middle School):

- Interior work progressed steadily, including floor grinding, electrical and plumbing finishes, and casework installation.
- Caulking and expansion joints were in progress throughout March.

High School Gymnasium:

- Casework, ceramic tile, door hardware, and electrical finishes were underway.
- Exterior work such as metal wall panels, gutters, and downspouts neared completion.





Bus Fueling & Sitework:

- Crews completed grading and started sidewalk prep and lighting rough-ins.
- Irrigation sleeves and landscaping prep were also underway toward the end of the month.

Drywall and Elevator:

- Drywall installation continued throughout enclosed areas of the classroom addition.
- The elevator install was completed, opening access to all floors for finish crews.



ACTIVITIES SCHEDULED FOR NEXT PERIOD

In April, work will focus on finishes and prepping exterior areas:

- **Classrooms:** Continue drywall, ceiling work, and interior finishes.
- **Gymnasium:** Begin flooring prep, continue with electrical systems for scoreboards and lighting.
- **Sitework:** Start curb, sidewalk, and paving operations; continue with lighting and landscaping infrastructure.
- **Exterior Finishes:** Wrap up remaining exterior sealing and detail work.
The project is now in a phase where visible progress accelerates as finish materials go in and systems are completed.

By keeping the schedule tight and maintaining strong coordination between different construction teams, we anticipate making significant progress throughout February, bringing the project another step closer to completion.



HIGHLIGHTS, CHALLENGES, SOLUTIONS

Ongoing Challenge:

Delays from PGE continue to impact the schedule for electrical underground work at the bus fueling area. This affects follow-on tasks like lighting, landscaping, and paving.



A key commitment of our project has been to engage and support the local economy by involving local vendors and contractors in the construction process. This month, we continued to honor that commitment, with a significant portion of our contracts awarded to businesses within the local community. This approach not only bolsters the local economy but also builds a sense of community ownership and pride in the project. It's a reflection of our belief that the best results come from working closely with those who share a direct stake in the success of our schools.

LOCAL VENDORS AND CONTRACTORS WORKING ON SCHOOL PROJECTS

- HMK Company
- Geotechnical Resources, Inc.
- TerraCalc Land Surveying
- Warrior Construction
- GT Landscape Solutions
- S&S Electrical
- Robert Lloyd Sheet Metal
- Soriano
- Southtown Glass
- Salem Heating & Sheet Metal
- JB Insulation
- Davidsons Masonry
- Valley Flooring
- Lile International
- Facet Architecture

